



DEPARTMENT OF PUBLIC WORKS  
 OFFICE OF THE CITY ENGINEER  
 605 E. End Blvd South  
 Marshall, Texas 75671  
 903-935-4489

**Project Startup Notice: 2022 Street Improvement Program**  
**PROJECT UPDATE: October 14, 2022**

**Project:** 2022 Street Improvement Program

**Description:** Includes the complete reconstruction, paving, striping, and signage upgrades, as necessary, of select distressed City roadways. Expect delays when crews are working on your roadway.

**Miles of Roadway in Project Pool:** 4.98± miles. Work performed under this program will include some or all of the listed roads with final scope of work to be determined based on bid prices and available funding.

**Anticipated Schedule:**

Advertisement: May 2022 - **COMPLETED**  
 Award of Contract: June 2022 - **COMPLETED**  
 Begin Construction: On or about August 19, 2022 **BEGUN**  
 Anticipated Completion: October, 2022

**Funding Sources:**

City Street Program\Dedicated Sales Tax

**Contact Information:**

For more information about this project, please feel free to contact Eric Powell, PE, City Engineer\Director of Public Works at the City of Marshall Public Works Department: 903-935-4489.



*Typical Paving Operations*

**PROJECT UPDATE AS OF OCTOBER 14, 2022:**

As of today, Friday October 14, 2022 the following Streets have been paved:

- Pemberton St from Billups to SL390 (MLK Blvd)
- Field St from Howard St to SL390 (MLK Blvd)
- Martin Lake Rd from HWY59 to I20 Frontage Rd.

The following streets are currently cement-treated and are schedule for overlay on Monday, October 17, 2022 weather permitting:

- Frank St from SL30 to Charlotte
- Charlotte St from Frank St to Fair St.

Unfortunately, the City was made aware of a problem at the supplier who provides the powdered Portland cement that is used for the second stage of reconstruction known as “cement-treated base.” This unfortunate circumstance has caused additional delays for the City’s paving contractor as he and his crews are working towards finishing the 2022 Street Improvement Program. As soon as the supplier informs our contractor that he can again receive the portland cement again, work will commence on those remaining streets that are waiting for the second stage and then paving can quickly follow,

## 2022 STREET IMPROVEMENT PROGRAM ROADLIST (4.98 MILES) WITH STATUS AS OF OCTOBER 14, 2022:

PCI Index	ST Pre	STREET NAME	ST Surf	FROM	TO	Length	Width (Avg)	Area	Tonnage	Current Status	Next Step	
19		ACADIA	ST	LAUREL ST	W CAROLANNE ST	344	36	1,376	158	CTB	Overlay	
25		AINSLEY	ST	E HOUSTON ST	E BOWIE ST	444	20	987	113	CTB	Overlay	
20	N	ALAMO	BLVD	REPOSE LN	GRAND AVE (HWY 80)	696	28	2,165	249	Pulverized	CTB	
24		ALBERT	ST	E HOUSTON ST	E TRAVIS ST	1205	24	3,213	370	Pulverized	CTB	
22		BOONE	ST	KARNACK HWY (HWY43)	E TEDDY ST	422	20	938	108		Pulverizing	
20		BRIMM	ST	BENITA ST	MURPHEY ST	866	28	2,694	310	CTB	Overlay	
23		CENTER	ST	WAUSAU ST	N FRANKLIN ST	365	20	811	93	Pulverized	CTB	
23		CHARLOTTE	ST	FRANK ST	FAIR ST	544	22	1,330	153	Pulverized	Overlay	
25	S	COLUMBUS	ST	E BOWIE ST	E FANNIN ST	301	22	736	85		Milling	
25	N	COLUMBUS	ST	REPOSE LN	GRAND AVE (HWY 80)	744	24	1,984	228		Milling	
20		ESPLANADE	AVE	EAST AVE	VALE ST	618	18	1,236	142			
21		FIELD	ST	HOWARD ST	SL390	867	20	1,927	222	Pulverized	Complete	
24		FORREST	TERR	BOMAR ST	S GROVE ST	274	20	609	70		Pulverizing	
25		FRANK	ST	SL390	CHARLOTTE ST	257	24	685	79	Pulverized	Overlay	
17		GREENWOOD	AVE	N ALAMO BLVD	N COLUMBUS ST	359	24	957	110	Pulverized	CTB	
17	N	GRISMORE	ST	KARNACK HWY (HWY43)	E TEDDY ST	517	20	1,149	132		Pulverizing	
25		HANKS	ST	ROBERTSON ST	SUMMITT ST	546	20	1,213	140	Pulverized	CTB	
25		HARGROVE	ST	SLEDGE ST	TOLIVAR ST	1161	24	3,096	356	Pulverized	CTB	
21	S	HAZELWOOD	ST	E HOUSTON ST	E TRAVIS ST	1196	22	2,924	336	Pulverized	CTB	
18		HIGHLAND	DR	S ALLEN BLVD	S CALLUM ST	510	18	1,020	117	Pulverized	CTB	
20		IDA	ST	HENDERSON ST	LAKE ST	836	24	2,229	256	Pulverized	CTB	
21		JOHN REAGAN	ST	JASPER DR	CADDO ST	837	30	2,790	321		Pulverizing	
15		LAKE	ST	GEORGIA ST	IDA ST	2448	22	5,984	688		Overlay	
16		LANE	ST	IDA ST	MAY ST	277	20	616	71	Pulverized	CTB	
23		LOUISIANA	ST	SUMMIT ST	POPLAR ST	603	22	1,474	170	Pulverized	CTB	
12	N	MARION	ST	MANES ST	KATHERINE ST	340	24	907	104	Pulverized	Overlay	
		MARTIN LAKE	RD	HWY59	20 FRONTAGE	4297	28	13,368	1,537	Overlay	Line Striping	
20		MOCKINGBIRD	LN	END	SANFORD ST	214	22	523	60		Pulverizing	
20		MORRISON	ST	HENDRIX ST	PARKER ST	1126	22	2,752	317	Pulverized	CTB	
15		ORIS	ST	SPEED ST	END	877	22	2,144	247	Pulverized	CTB	
21		REPOSE	LN	N ALAMO BLVD	N COLUMBUS ST	357	20	793	91	Pulverized	CTB	
17		ROBERTSON	ST	HANKS ST	SLEDGE ST	338	18	676	78	Pulverized	CTB	
15		SANFORD	ST	W EMORY ST	MOCKINGBIRD ST	656	22	1,604	184		Pulverizing	
17		TALLIAFERRO	ST	HARGROVE ST	SEDBERRY ST	550	20	1,222	141	Pulverized	CTB	
23		WAUSAU	ST	CENTER ST	W WRIGHT ST	310	22	758	87	Pulverized	CTB	
25		PEMBERTON	ST	BILLUPS ST	SL390	2271	24	6,056	696	Pulverized	Complete	
<b>TOTALS:</b>									<b>74,946</b>	<b>8,619</b>		
<b>LEGEND:</b>												
Cement Treated Base (CTB), waiting on Overlay												
Overlay complete, waiting on Line Striping												
Pulverized, waiting on CTB then Overlay												
Waiting on Pulverization, then CTB												
Concrete base found, waiting on Milling then Overlay												
2" watermain found, delayed until 2023												

**PROJECT PHOTOS – September 13, 2022.**

1. Albert St. from E Houston St. to E Travis St.



*Albert St. reconstructed, waiting on cement treatment.*

2. Greenwood Ave from N Alamo to N Columbus.




*Greenwood Ave reconstructed, waiting on cement treatment.*

3. Hazelwood from E Houston to E Travis



*Showing cement treatment*

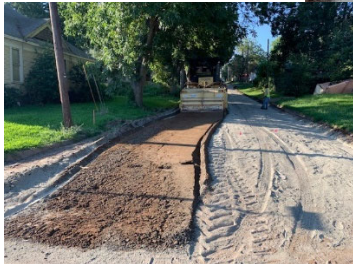

*Machine mixing pulverized soil with Portland cement*

4. Repose Ln from N Alamo to N Columbus



*Pulverized, waiting on cement treatment*
